




# Northeast Ohio Regional Sewer District

## Daily Precipitation Report Sunday, November 22, 2020

Accumulation in inches

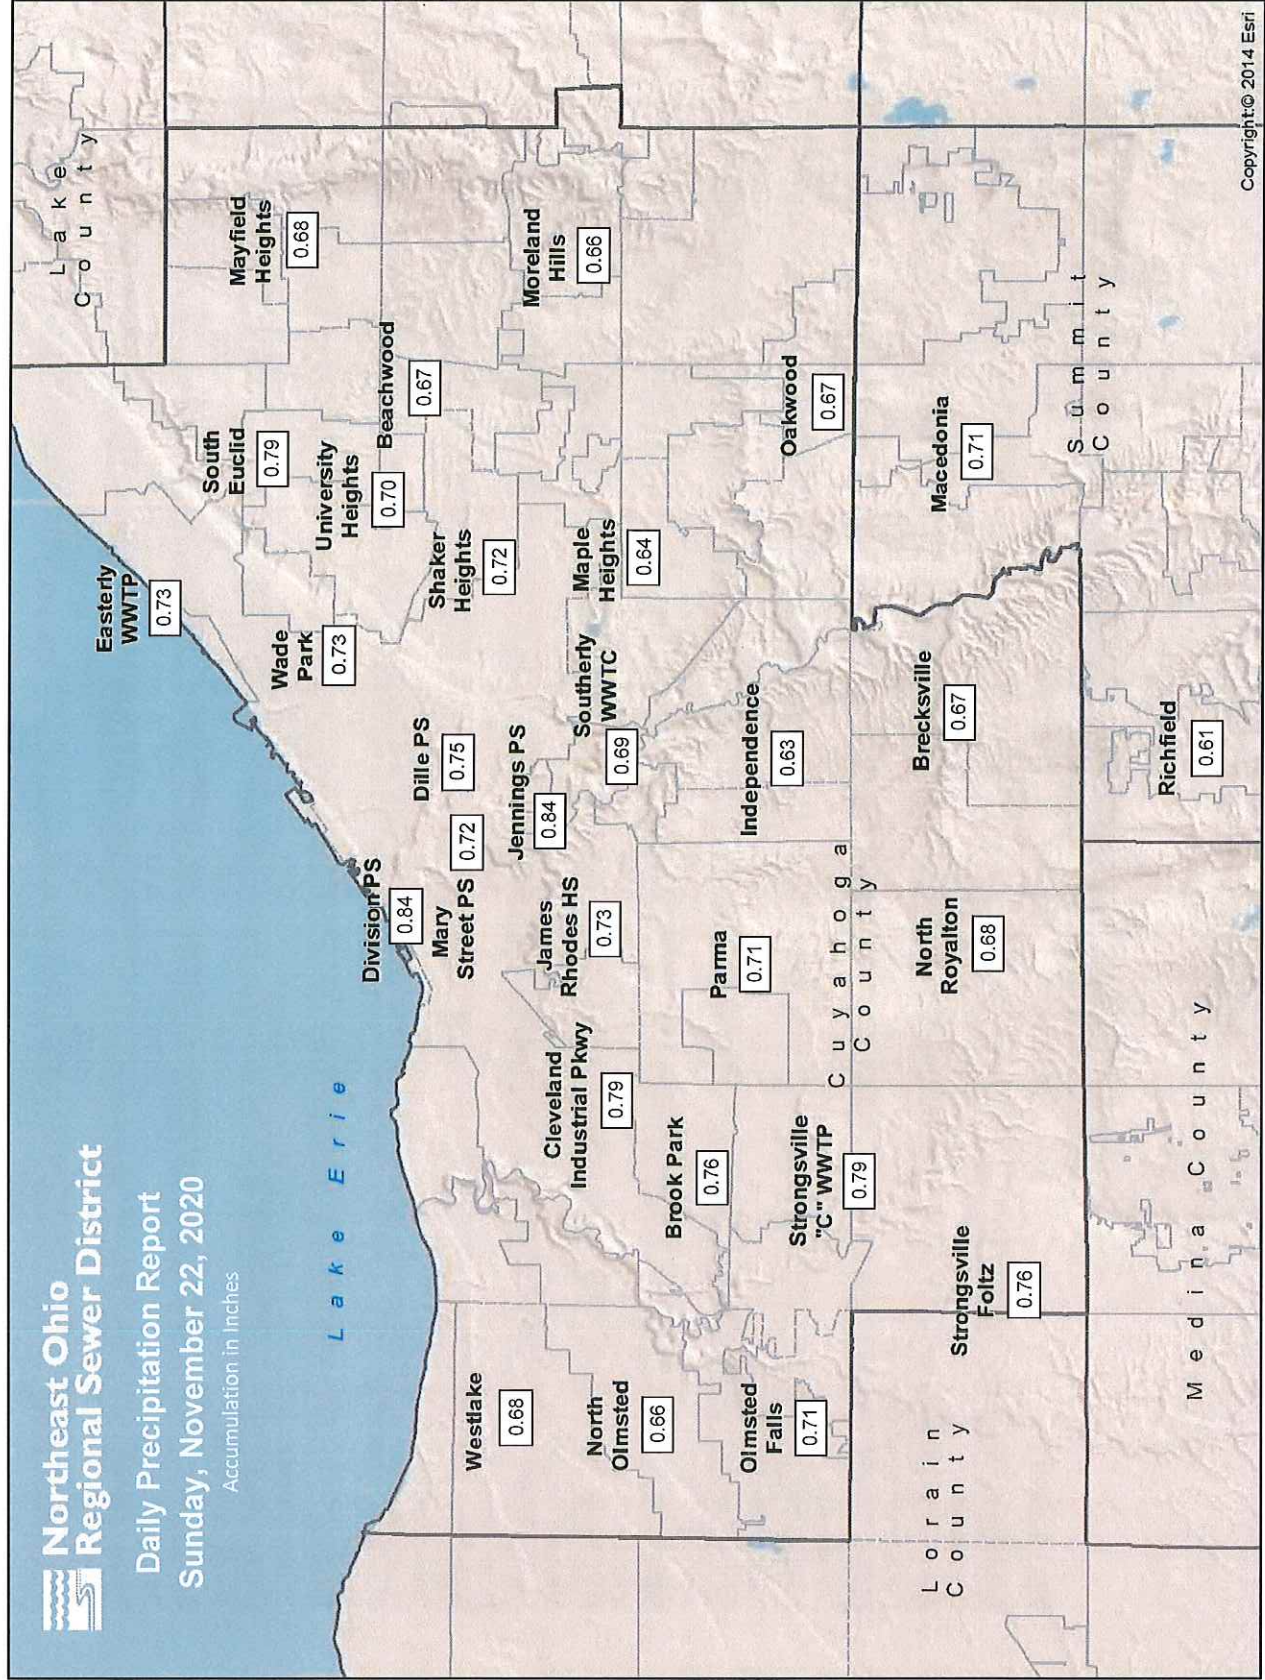

# Northeast Ohio Regional Sewer District

## Daily Precipitation Report

Sunday, November 22, 2020

Site Location	Peak Accumulation (Inches)				
	24-Hour	6-Hour	3-Hour	1-Hour	5-Minute
Beachwood	0.67	0.45	0.32	0.13	0.02
Brecksville	0.67	0.59	0.46	0.27	0.08
Brook Park	0.76	0.58	0.41	0.17	0.03
Cleveland Industrial Pkwy	0.79	0.57	0.40	0.16	0.02
Dille Ave PS	0.75	0.54	0.37	0.15	0.02
Division Ave PS	0.84	0.60	0.41	0.17	0.02
Easterly WWTP	0.73	0.50	0.32	0.14	0.02
Independence	0.63	0.50	0.35	0.14	0.03
James Rhodes HS	0.73	0.55	0.39	0.16	0.03
Jennings PS	0.84	0.60	0.42	0.17	0.03
Macedonia	0.71	0.64	0.50	0.26	0.04
Maple Heights	0.64	0.49	0.34	0.14	0.03
Mary Street PS	0.72	0.53	0.36	0.14	0.03
Mayfield Heights	0.68	0.45	0.32	0.13	0.02
Moreland Hills	0.66	0.56	0.42	0.22	0.04
North Olmsted	0.66	0.48	0.33	0.13	0.02
North Royalton	0.68	0.55	0.39	0.18	0.04
Oakwood	0.67	0.58	0.44	0.24	0.04
Olmsted Falls	0.71	0.54	0.38	0.15	0.03
Parma	0.71	0.53	0.37	0.13	0.03
Richfield	0.61	0.59	0.48	0.25	0.04
Shaker Heights	0.72	0.51	0.35	0.14	0.02
South Euclid	0.79	0.55	0.38	0.16	0.03
Southerly WWTC	0.69	0.51	0.36	0.14	0.03
Strongsville C WWTP	0.79	0.59	0.41	0.15	0.03
Strongsville Foltz	0.76	0.57	0.39	0.14	0.03
University Heights	0.70	0.50	0.34	0.14	0.03
Wade Park	0.73	0.50	0.34	0.13	0.02
Westlake	0.68	0.46	0.28	0.12	0.02

## Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

<b>WO Number:</b> 201125-0004	<b>Category:</b> SSOs
<b>Status:</b> Complete	<b>Problem:</b> Storm Response
<b>Status Date:</b> 11/30/2020 10:03 am	<b>Main Task:</b> Inspection
<b>Asset:</b> SSO 431	
<b>Location:</b> FAIRFAX AT NORTH PARK	
<b>Cause:</b> Weather	<b>Assigned By:</b>
<b>Assigned Crew:</b>	<b>Assigned Date:</b>
<b>Supervisor:</b> Jackson, Jeff	<b>Start Date:</b> 11/25/2020 8:00 AM
<b>Lead Worker:</b> DelZoppo, Michael	<b>End Date:</b> 11/25/2020
<b>Priority:</b> High	<u>Override</u>
<b>Account #:</b>	<u>Notifications</u>
<b>Proj No - Acct:</b>	Problem <input type="checkbox"/>
<b>Project:</b>	Overdue <input type="checkbox"/>
<b>Reason:</b>	Lead Worker <input type="checkbox"/>
<b>Received By:</b>	Task <input type="checkbox"/>
<b>Inspected By:</b>	Supervisor <input type="checkbox"/>
	Hard Lock WO <input type="checkbox"/>

### Request Comments for Work Order

Inspect all (45) SSO's when rainfall is one quarter (1/4") inch or higher.

### Location

**Department:** Sewer Collection  
**Division:** Sewer Collection  
**Sub-Division:**  
**Area:**  
**Sub-Area:**  
**Owner:**  
**Location:**  
**Classification:**

**Maintenance Zone:****Alternate Zone:**

### Comments for Crew

Inspect all (45) SSO's when rainfall is one quarter (1/4") inch or higher.

### Work Order Locations

<u>Address</u>	<u>Address 2</u>
<u>X Coord</u>	<u>Y Coord</u>
<u>General Location</u>	
FAIRFAX AT NORTH PARK	
2,220,655.65435414	665,517.24643672
DOAN BROOK	
NORTH PARK AND COVENTRY	
2,219,873.16674590	666,048.82312946
DOAN BROOK - MAIN BRANCH	
FAIRMOUNT SOUTH OF SCARBOROUGH	
2,220,364.86097248	666,446.72325230
DOAN BROOK - MAIN BRANCH	
FAIRMOUNT AT FAIRFAX	
2,220,920.81917815	666,080.57995571
DOAN BROOK - MAIN BRANCH	
FAIRMOUNT AT NORTH WOODLAND (S. SIDE)	
2,223,053.81655256	664,693.25202172
DOAN BROOK - MAIN BRANCH	
3012 NORTH WOODLAND	
2,222,845.06631389	664,689.08536339
DOAN BROOK	
2,226,440.21168265	664,329.55524255
2,226,354.79813956	664,409.89202413
2,226,389.92077273	664,379.07548472
FAIRMOUNT AT DARTMOOR	
2,225,149.97508989	664,453.31024438
DOAN BROOK - MAIN BRANCH	
FAIRMOUNT AT WELLINGTON	
2,223,969.26550905	664,532.08075613
DOAN BROOK - MAIN BRANCH	

**Work Order Detail Report**

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

FAIRMOUNT AT NORTH WOODLAND (N. SIDE)		
2,223,111.44143730	664,794.46048072	DOAN BROOK - MAIN BRANCH
FAIRMOUNT AT MARLBORO		
2,221,638.88762389	665,726.15513962	DOAN BROOK - MAIN BRANCH
FAIRMOUNT AT ARLINGTON		
2,222,127.85875881	665,393.74077822	DOAN BROOK - MAIN BRANCH
FAIRMOUNT & COVENTRY (SCARBOROUGH)		
2,220,278.63411081	667,231.62916280	DOAN BROOK - MAIN BRANCH
FAIRMOUNT AND COVENTRY		
2,220,419.37169023	666,567.10752596	DOAN BROOK - MAIN BRANCH
SCARBOROUGH AT LAMBERTON		
2,221,598.28993607	666,996.61322863	
MONMOUTH, EAST OF DARTMOOR		
2,225,152.08663423	665,499.19660404	DOAN BROOK
BRADFORD AND LEE		
2,224,643.84191582	665,970.39907372	DOAN BROOK - MAIN BRANCH
EDDINGTON		
2,221,299.08384156	674,932.84604380	
HAMPSHIRE LANE AT MAYFIELD (18")		
2,219,348.17140481	672,922.02624655	DUGWAY CREEK - MAIN BRANCH
EAST OVERLOOK AT EDGEHILL		
2,218,479.60588473	671,538.70289771	DOAN BROOK - MAIN BRANCH
HAMPSHIRE LANE AT MAYFIELD (36")		
2,219,354.97683740	672,902.85961822	DUGWAY CREEK - MAIN BRANCH
2600 HAMPSHIRE RD		
HAMPSHIRE AT EUCLID HTS. BLVD.		
2,218,465.44876081	671,703.91811846	DOAN BROOK - MAIN BRANCH
CEDAR BTW. FAIRMOUNT/DEMINGTON		
2,218,036.25112839	669,668.09115338	DOAN BROOK - MAIN BRANCH
2828 BERKSHIRE, EAST OF COVENTRY		
2,220,768.48319674	670,614.63814481	DUGWAY CREEK - MAIN BRANCH
3003 EUCLID HEIGHTS BLVD		
2,222,538.05642922	672,458.71614955	DUGWAY CREEK - MAIN BRANCH
South Taylor between Antisdale Ave and Superior Rd		
2,227,113.30810548	671,276.67684697	
LEE RD. & SUPERIOR AVE.		
2,224,449.07983814	672,366.92072946	HEIGHT = NA, WIDTH = NA, LENGTH = NA
EUCLID HEIGHTS BLVD AND LEE		
2,224,196.49208874	673,102.72798488	DUGWAY CREEK - MAIN BRANCH
EUCLID HEIGHTS BLVD/CUMBERLAND		
2,223,890.24106081	672,984.80925746	DUGWAY CREEK - MAIN BRANCH
1685 CUMBERLAND		
2,223,414.40769489	674,158.55920655	DUGWAY CREEK - MAIN BRANCH
CUMBERLAND/SOMERTON		
2,223,678.60992239	673,517.13791722	DUGWAY CREEK - MAIN BRANCH
2225 NOBLE RD		
2225 NOBLE ROAD		
2,227,020.20068015	682,910.03907888	NINE MILE CREEK - MAIN BRANCH
QUILLIAMS, N. OF RANDOLF		
2,229,594.65878581	682,393.53289405	NINE MILE CREEK - MAIN BRANCH
LANGTON AND ATHERSTONE		
2,228,126.76638040	684,188.23206055	
2,220,777.89623564	666,181.72575080	
2,218,501.67473823	671,997.54581206	
2,216,759.55453481	670,474.59347738	

## Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

2,224,536.21778722	668,887.44048372
2,226,741.35609348	679,432.95121680
2,226,591.76420106	679,420.92761880
2,227,825.14395215	684,881.15948047

# Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

Work Order Assets						
Object Type	Description 1		Description 2		Asset ID	Completed
System ID 1	System ID 2	Odometer	Hourmeter	Othermeter		
Sewer Control Valve					FAIRFAX AT NORTH PARK	
SSO 431					26	
Sewer Control Valve					NORTH PARK AND COVENTRY	
SSO 114					16	
Sewer Control Valve					FAIRMOUNT SOUTH OF SCARBOROUGH	
SSO 121					35	
Sewer Structure						
SA16AAWB0					3094	
Sewer Control Valve					FAIRMOUNT AT FAIRFAX	
SSO 112					7	
Sewer Control Valve					FAIRMOUNT AT NORTH WOODLAND (S. SIDE)	
SSO 99					6	
Sewer Control Valve					3012 NORTH WOODLAND	
SSO 432					14	
Sewer Control Valve						
DB-03					55	
Sewer Control Valve						
DB-01					56	
Sewer Control Valve						
DB-02					57	
Sewer Control Valve					FAIRMOUNT AT DARTMOOR	
CH-04					5	
Sewer Control Valve					FAIRMOUNT AT WELLINGTON	
SSO 110					44	
Sewer Control Valve					FAIRMOUNT AT NORTH WOODLAND (N. SIDE)	
SSO 87					33	
Sewer Control Valve					FAIRMOUNT AT MARLBORO	
SSO 116					4	
Sewer Control Valve					FAIRMOUNT AT ARLINGTON	
SSO 111					46	
Sewer Control Valve					FAIRMOUNT & COVENTRY (SCARBOROUGH)	
SSO 113					37	
Sewer Control Valve					FAIRMOUNT AND COVENTRY	
SSO 124					47	
Sewer Control Valve					SCARBOROUGH AT LAMBERTON	
CH-50					53	
Sewer Control Valve					BRADFORD AND LEE	
SSO 129					11	
Sewer Control Valve					EDDINGTON	
CH-52					2	
Sewer Control Valve					HAMPSHIRE LANE AT MAYFIELD (18")	
SSO 88					42	
Sewer Control Valve					EAST OVERLOOK AT EDGEHILL	
SSO 122					36	
Sewer Control Valve					HAMPSHIRE LANE AT MAYFIELD (36")	
SSO 89					34	
Sewer Structure						
SA16ADZB0					1536	
Sewer Control Valve					HAMPSHIRE AT EUCLID HTS. BLVD.	
SSO 91					20	
Sewer Structure						
SA16ADPH0					4446	
Sewer Control Valve					CEDAR BTW. FAIRMOUNT/DEMINGTON	
SSO 120					8	
Sewer Control Valve					2828 BERKSHIRE, EAST OF COVENTRY	

\* A 'Hidden' field indicates permission to view the secured field is turned off.

WO#: 201125-0004



**Work Order Detail Report**

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

SSO 103	19
Sewer Control Valve	3003 EUCLID HEIGHTS BLVD
SSO 104	15
Sewer Structure	
SA16AGMG0	3402
Sewer Control Valve	South Taylor between Antisdale Ave and Superior R
CH-30	52
Sewer Control Valve	LEE RD. & SUPERIOR AVE.
DV-11	9
Sewer Control Valve	EUCLID HEIGHTS BLVD AND LEE
SSO 108	22
Sewer Control Valve	EUCLID HEIGHTS BLVD/CUMBERLAND
SSO 106	43
Sewer Control Valve	1685 CUMBERLAND
SSO 95	18
Sewer Control Valve	CUMBERLAND/SOMERTON
SSO 105	30
Sewer Structure	
SA16AQD0	4987
Sewer Structure	
SA16AQQC0	3745
Sewer Control Valve	2225 NOBLE ROAD
SSO 102	3
Sewer Control Valve	QUILLIAMS, N. OF RANDOLF
SSO 107	38
Sewer Control Valve	LANGTON AND ATHERSTONE
CH-51	54
Sewer Structure	
SA16APEF0	1809

**Work Order Detail Report**

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

Check List				
Item	Completed	Condition	Completion Date/Time	Est Completion Date
1 A-37-FAIRFAX AT NORTH PARK SA16ACPG0	<input type="checkbox"/>	Sound	11/25/2020/ 7:51 am	
No overflow				
2 A-36-NORTH PARK AT COVENTRY SA16ACNB0 (IN MEDIAN-CEMENT)	<input type="checkbox"/>	Sound	11/25/2020/ 7:54 am	
No overflow				
3 A-45-FAIRMOUNT ( IN THE ISLAND EAST OF COVENTRY) SA16ACNE0	<input type="checkbox"/>	Sound	11/25/2020/ 7:56 am	
No overflow				
4 A-54-2806 FAIRMOUNT SA16AAWB0 (TREE LAWN BY SIDEWALK)	<input type="checkbox"/>	Sound	11/25/2020/ 7:58 am	
No overflow				
5 A-33-FAIRMOUNT AT FAIRFAX SA16AAWC0 (SW CORNER IN THE SIDEWALK)	<input type="checkbox"/>	Sound	11/25/2020/ 7:59 am	
Overflowed				
6 A-39-3012 NORTH WOODLAND SA16AAWM5 (TREE LAWN)	<input type="checkbox"/>	Sound	11/25/2020/ 8:03 am	
No overflow				
7 A-2 FAIRMOUNT AT NORTH WOODLAND SA16AAWK0(MIDDLE OF THE ROAD)	<input type="checkbox"/>	Sound	11/25/2020/ 8:04 am	
No overflow				
8 A-6 FAIRMOUNT AT SHELBURNE ST16ZBJK0 (WEST BOUND LANE)	<input type="checkbox"/>	Sound	11/25/2020/ 8:07 am	
No overflow				
9 A-5 FAIRMOUNT AT SHELBURNE SA16AAXB0(ON THE SE CORNER IN THE SIDEWALK)	<input type="checkbox"/>	Sound	11/25/2020/ 8:08 am	
Overflowed				
10 A-7 FAIRMOUNT AT SHELBURNE SA16AAVH0 (EAST BOUND)	<input type="checkbox"/>	Sound	11/25/2020/ 8:09 am	
Overflowed				
11 A-4 FAIRMOUNT AT DARTMOOR SA16AAVB0(NW CORNER IN THE GRASS BY STOP SIGN)	<input type="checkbox"/>	Sound	11/25/2020/ 8:13 am	
No overflow				
12 A-3 FAIRMOUNT AT WELLINGTON SA16AAUW0 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:15 am	
No overflow				
13 A-1 3041 FAIRMOUNT SA16AAUT0 (TREE LAWN NEAR SIDEWALK)	<input type="checkbox"/>	Sound	11/25/2020/ 8:16 am	
No overflow				
14 A-32 FAIRMOUNT AT ARLINGTON SA16AAUP0 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:19 am	
No overflow				
15 A-38 FAIRMOUNT AT MARLBORO SA16AAUM0 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:20 am	
No overflow				
16 A-49 2757 FAIRMOUNT SA16AAUC0 (EAST OF CHURCH IN TREE LAWN)	<input type="checkbox"/>	Sound	11/25/2020/ 8:21 am	
No overflow				
17 A-35 2393 COVENTRY SA16AASK0 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:22 am	
No overflow				
18 A-50 SCARBOROUGH AND LAMBERTON SA16AANE5 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:25 am	
No overflow				

\* A 'Hidden' field indicates permission to view the secured field is turned off.

WO#: 201125-0004



# Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

19	A-47 2528 STRATFORD SA16ACDB5 (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:27 am
	No overflow			
20	A-57 E MONMOUTH SA16AFWA5 WEST OF (DARTMOOR NEAR LEE)	<input type="checkbox"/>	Sound	11/25/2020/ 8:29 am
	No overflow			
21	A-58 E MONMOUTH AT EXETER (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:30 am
	No overflow			
22	A-9 BRADFORD AT LEE SA16AFLLO (INTERSECTION)	<input type="checkbox"/>	Sound	11/25/2020/ 8:32 am
	Overflowed			
23	B-52 EDDINGTON NORTH OF AVONDALE SA16AHVE0	<input type="checkbox"/>	Sound	11/25/2020/ 8:40 am
	No overflow			
24	B-10 HAMPSHIRE LANE AT MAYFIELD SA16BACB0	<input type="checkbox"/>	Sound	11/25/2020/ 8:43 am
	No overflow			
25	B-11 HAMPSHIRE LANE AT MAYFIELD SA16AEEA0	<input type="checkbox"/>	Sound	11/25/2020/ 8:44 am
	No overflow			
26	B-61 2600 HAMPSHIRE SA16ADZB0	<input type="checkbox"/>	Sound	11/25/2020/ 8:45 am
	No overflow			
27	HAMPSHIRE AT EUCLID HTS. BLVD. SA16ADPR0	<input type="checkbox"/>	Sound	11/25/2020/ 8:47 am
	No overflow			
28	B-46 EDGEHILL AT E OVERLOOK SA16AEPF0	<input type="checkbox"/>	Sound	11/25/2020/ 8:48 am
	No overflow			
29	B-42 12537 CEDAR SA16ACZA0	<input type="checkbox"/>	Sound	11/25/2020/ 8:53 am
	No overflow			
30	B-15 COVENTRY AND CEDAR SA16ADBHO	<input type="checkbox"/>	Sound	11/25/2020/ 8:55 am
	No overflow			
31	B-23 2828 BERKSHIRE SA16AETA0	<input type="checkbox"/>	Sound	11/25/2020/ 8:58 am
	No overflow			
32	B-24 3003 EUCLID HTS. BLVD. ST16AALB0	<input type="checkbox"/>	Sound	11/25/2020/ 9:01 am
	No overflow			
33	B-56 LEE AND MEADOWBROOK SA16AGMG0	<input type="checkbox"/>	Sound	11/25/2020/ 9:07 am
	Overflowed			
34	C-30 S TAYLOR NORTH OF SUPERIOR SA16AIVF0	<input type="checkbox"/>	Sound	11/25/2020/ 9:13 am
	Overflowed			
35	C-12 LEE AND SUPERIOR SA16AGTJ0	<input type="checkbox"/>	Sound	/ 9:17 am
	No overflow			
36	C-28 EUCLID HTS. BLVD AND LEE RD SA16AGTE0	<input type="checkbox"/>	Sound	11/25/2020/ 9:18 am
	No overflow			
37	C-26 EUCLID HTS BLVD AND CUMBERLAND SA16AIRLO	<input type="checkbox"/>	Sound	11/25/2020/ 9:19 am
	No overflow			
38	C-25 CUMBERLAND AND SOMERTON SA16AISA0	<input type="checkbox"/>	Sound	11/25/2020/ 9:22 am
	No overflow			
39	C-17 1685 CUMBERLAND RD SA16AQIB0	<input type="checkbox"/>	Sound	11/25/2020/ 9:23 am
	No overflow			

\* A 'Hidden' field indicates permission to view the secured field is turned off.

WO#: 201125-0004

**Work Order Detail Report**

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

40	C-59 3427 THORNE RD SA16AQD0	<input type="checkbox"/>	Sound	11/25/2020/ 9:29 am
No overflow				
41	C-60 3415 THORNE RD SA16AQQC0	<input type="checkbox"/>	Sound	11/25/2020/ 9:30 am
No overflow				
42	C-22 2225 NOBLE RD ST16ZLHB0	<input type="checkbox"/>	Sound	11/25/2020/ 9:34 am
No overflow				
43	C-27 QUILLIAMS NORTH OF RANDOLPH SA16AOUQ0	<input type="checkbox"/>	Sound	11/25/2020/ 9:38 am
No overflow				
44	C-51 ATHERSTONE AND LANGTON SA16AOKA0	<input type="checkbox"/>	Sound	/ 11/25/2020
Can't inspect.				
45	C-50 3593 FENLEY SA16APEH0	<input type="checkbox"/>	Sound	11/25/2020/ 9:40 am
No overflow				

**Tasks/Resources****SWCT27 Inspection****Crew:**

Supervisor: Ferrone, Anthony

**Status:**

UOM: Each

\*Cal'c UC: \$6.21

# of Units: 45.00

\*Task Cost: \$279.52

\*Unit Cost: \$0.00

Start Dt:

End Dt:

**Employee**

Resource	UOM	Units	*Total Cost	Alt Description	Start Dt	End Dt
9512 DelZoppo, Michael	Hours	8.00	\$172.32			

**Equipment**

Resource	UOM	Units	*Total Cost	Alt Description	Start Dt	End Dt
CHFLT50 FORD F250 CREW CAB 5	Hours	8.00	\$107.20			

Task Comment: SSO INSPECTION 0.70 INCHES OF RAIN

Projected Complete:

Lock: ☐

Repair Type:

Subcontractor:

Profit Center:

Quantity: 0.00

Lock: ☐

Unit of Measure: Each

\*Unit Cost: \$0.00

WO Hours: 0.00

	*Actual	*Estimated	*Difference
WO Duration	0.00	0.00	0.00
Labor Hours	8.00	0.00	0.00
Labor Costs	\$172.32	\$0.00	\$0.00
Material Costs	0.00	0.00	0.00
Fluids Costs	0.00	0.00	0.00
Equipment Costs	107.20	0.00	0.00
Contractor Costs	0.00	0.00	0.00
Misc. Costs	0.00	0.00	0.00
Total Costs	\$279.52	\$0.00	\$0.00

Use Task Info:

True

True

**Billing****Billed Party**

Customer ID:

Customer Name:

Address:

City:

State:

Zip:

Customer Number:

Last Name:

Phone:

Cell #:

Fax #:

E-mail:

**Billing Data**

Contact Name:

Invoice Number:

Incoming Account #:

\*Billing Amount:

Date Bill Sent:

Payment Received:

Payment Method:

Billing Required: ☐Billing Processed: ☐Imported to Financials: ☐**Associated PMs****PM Code and Description**  
SSO-02 SSO INSPECTION**Closed**

## Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

Tracking				
Item	Description	By	Date	Time
Work Order Creation	From Routine Work SSO-02 - SSO INSPECTION	jjackson	11/25/2020	12:02 PM
Supervisor Notification	Email Queued Successfully!	jjackson	11/25/2020	12:03 PM
Email Successfully Sent	jjackson@clvhts.com Lucity Work Order Update - Supervisor	BackgroundTaskUser	11/25/2020	12:03 PM
Status Change	From New Work Order to Complete	aferrone	11/30/2020	10:03 AM

Rates:	Opened At:	Televised:	<input type="checkbox"/>
Recieved By:	Pipe Footage Cleaned :	Power Rooter:	<input type="checkbox"/>
Work From:	Gallons Used:	Jet:	<input type="checkbox"/>
Pipe Size:	WO User 23:	Gap Vac:	<input type="checkbox"/>
Pipe Condition:	WO User 24:	Dye Test:	<input type="checkbox"/>
Could Not Open:	WO User 9:	Gap Root Cut:	<input type="checkbox"/>
Additional Repair:	User 10:	GIS Correction?:	<input type="checkbox"/>
Dye Test Reason:	Appointment Date DNL	WO User 30:	<input type="checkbox"/>
Test Performed Throug	Appointment Date: 11/25/2020 7:30 AM		
Dye Test Results:			
WO User 51:			
Measurement:	E Mail:		
History:	WO User 22:		

Manhole Basin Repair:	Pipe Size:
Material Used:	PVC Tees, Angles, Slec
Pipe Repair:	WO User 44:
Street Repair:	WO User 45:
Grass Repair:	WO User 46:
Curb Repair:	
Driveway- Sidewalk Re	
Construction Crew:	
WO User 39:	
WO User 40:	OUPS #:
WO User 41:	WO User 48:

WO User 52:	WO User 62:	
WO User 53:	WO User 63:	
WO User 54:	WO User 64:	
WO User 55:	WO User 65:	
WO User 56:	WO User 66:	
WO User 57:	WO User 67:	
WO User 58:	WO User 68:	
WO User 59:	WO User 69:	
WO User 60:	WO User 70:	
WO User 61:	WO User 71:	
WO User 72:	WO User 82:	Televised: <input type="checkbox"/>
WO User 73:	Quantity:	Paid: <input type="checkbox"/>
WO User 74:	WO User 84:	WO User 104: <input type="checkbox"/>
WO User 75:	WO User 85:	WO User 105: <input type="checkbox"/>
WO User 76:	WO User 86:	WO User 106: <input type="checkbox"/>

WO User 92 Date:	WO User 97 Date:
WO User 93 Date:	WO User 98 Date:
WO User 94 Date:	WO User 99 Date:
WO User 95 Date:	WO User 100 Date:
WO User 96 Date:	WO User 101 Date:

## Work Order Detail Report

11/30/2020

SSO INSPECTION 11-22-2020 0.70 INCHES OF RAIN

10:07 AM

WO User 77:	WO User 87:	WO User 107:	<input type="checkbox"/>
WO User 78:	WO User 88:	WO User 108:	<input type="checkbox"/>
WO User 79:	WO User 89:	WO User 109:	<input type="checkbox"/>
WO User 80:	WO User 90:	WO User 110:	<input type="checkbox"/>
WO User 81:	WO User 91:	WO User 111:	<input type="checkbox"/>
WO Creator: jjackson	WO Creation Date: 11/25/2020	PM Trigger:	Rec #: 6165
